BILL OF MATERIALS	ASSEMBLY POS. 2-R14			No. Required 1		POS. NO. 163
POS. NO.	QTYN.	Profile	LENGTH (mm)	Material	UNIT weight kg/m	weight (kg) QTY.	TOTAL	NOTE
163	1	IPE350-J	11954.9	S235JR	49.40	590.57	590.57	
176	1	IPE350-J	2000.0	S235JR	49.40	98.80	98.80	
237	1	PL20*180	720.0	S235JR	20.35	20.35	20.35	
240	1	PL20*180	510.0	S235JR	14.41	14.41	14.41	
413	2	PL10*80	150.0	S235JR	0.46	0.46	0.92	
490	10	PL5*75	75.0	S235JR	0.22	0.22	2.16	
491	9	PL5*130	180.0	S235JR	0.92	0.92	8.27	
501	9	PL5*100	100.0	S235JR	0.20	0.20	1.77	
Total Weight						737.0	(kg)	

BOLT, NUT & WASHERS MATERIAL LIST					
EACH	REMARK			UNIT WEIGHT KG/1000	WEIGHT (KG)
12	M 24x 70	BOLTS	GR8.8	343.0	4.12
12	M 24	NUTS	GR8.8	104.0	1.25
12	M 24	WASHERS	GR8.8	32.0	0.38
Total weight					5.75 (KG)

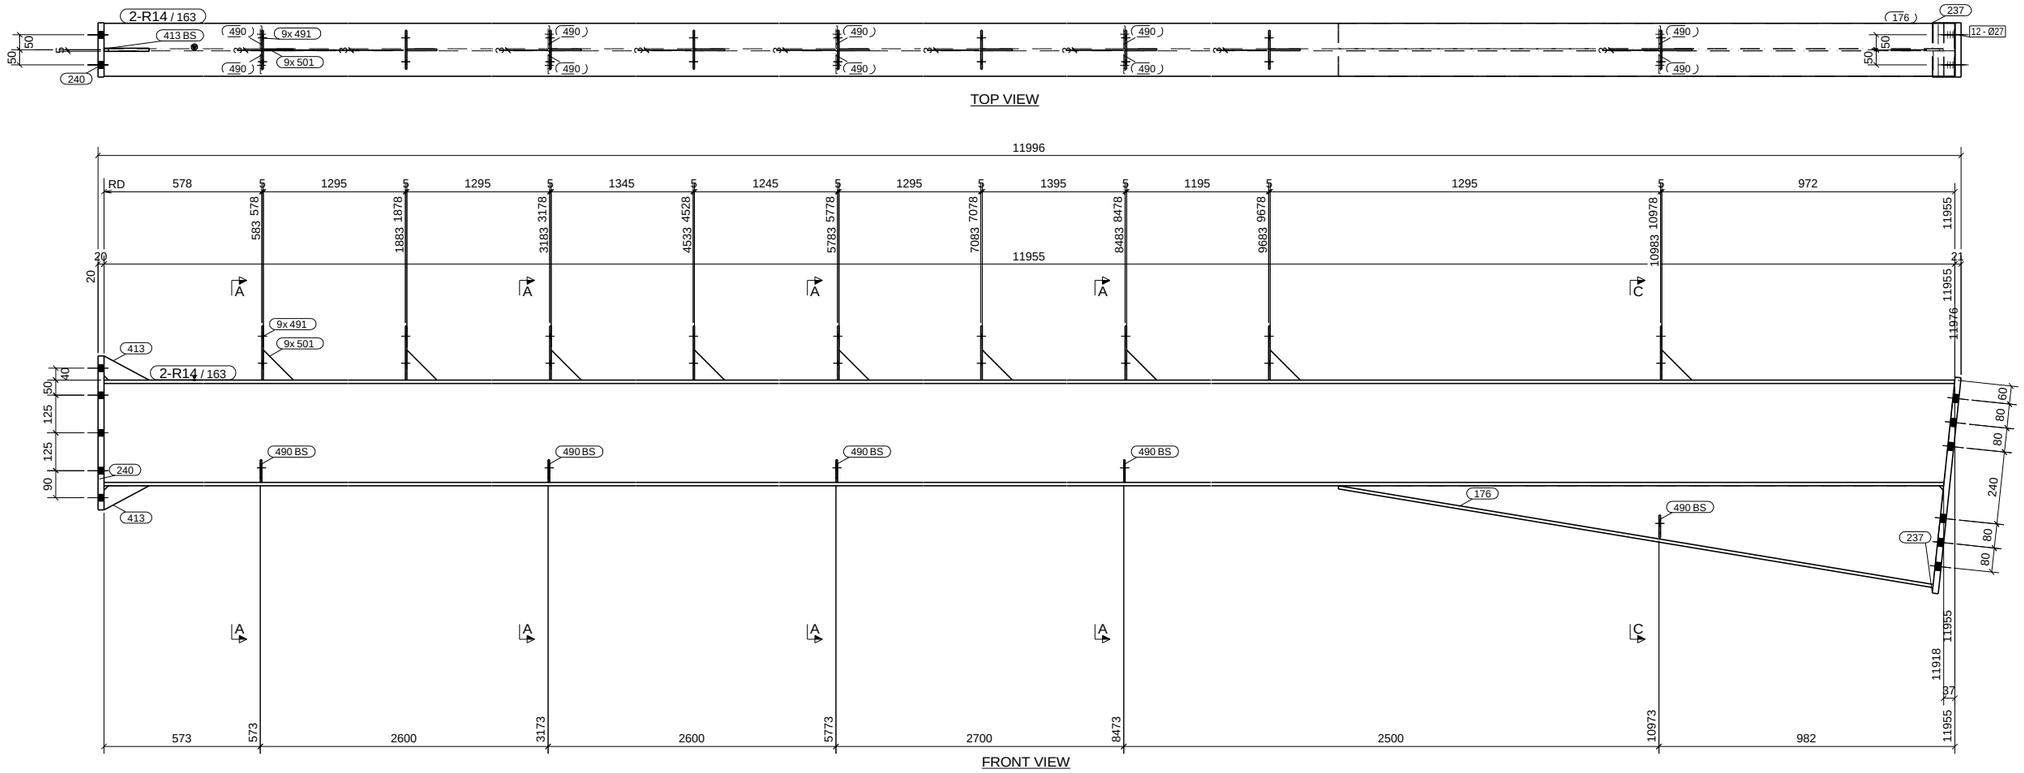

GENERAL NOTES:

1. ALL HOLES ARE 22 mm DIA (UON).
2. ALL DIMENSIONS ARE IN MM (UON).
3. UNLESS OTHERWISE NOTED ALL FILLET WELD SIZE SHALL BE 7mm FILLET CONTINUOUS(UON)
4. RD DENOTES BASE LINE = 00

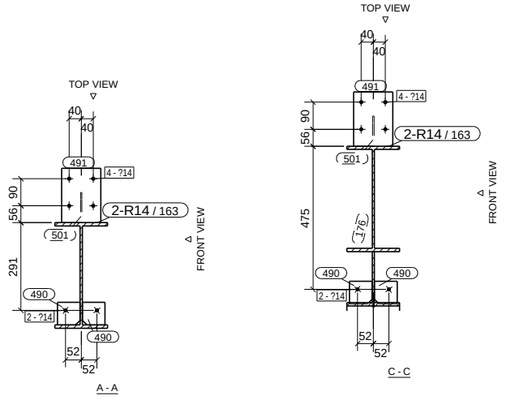

MARK: 2-R14
QTY: 1
DESC.: IPE350-J

REV.	DATE	DESCRIPTION	DRN	CHK	DSN

PROJECT NAME:

MADAR GROUP JORDAN

CONTRACTOR:

- - - - - - - - - - - - - - - - - - -

DRAWING TITLE:

RAFTER
2-R14

CHECKED BY	A.A	SCALE	
DATE	A.A	SHEET NO.	

Tekla structures
/12/2026 * 15:33:23

PDF created with pdfFactory Pro trial version www.pdffactory.com
