BILL OF MATERIALS		ASSEMBLY POS. 2-R58			No. Required 1		POS. NO. 432	
POS. NO.	QTYN.	Profile	LENGTH (mm)	Material	UNIT weight kg/m	weight (kg) QTY.	TOTAL	NOTE
432	1	IPE300-J	6043.1	S235JR	36.70	221.78	221.78	
253	2	PL15*170	320.0	S235JR	6.41	6.41	12.81	
491	2	PL5*130	180.0	S235JR	0.92	0.92	1.84	
511	2	PL5*70	100.0	S235JR	0.14	0.14	0.27	
Total Weight						236.8	(kg)	

BOLT, NUT & WASHERS MATERIAL LIST					
EACH	REMARK			UNIT WEIGHT KG/1000	WEIGHT (KG)
12	M20x60	BOLTS	GR8.8	204.2	2.45
12	M20	NUTS	GR8.8	59.8	0.72
12	M20	WASHERS	GR8.8	17.0	0.20
Total weight					3.37 (KG)



TOP VIEW

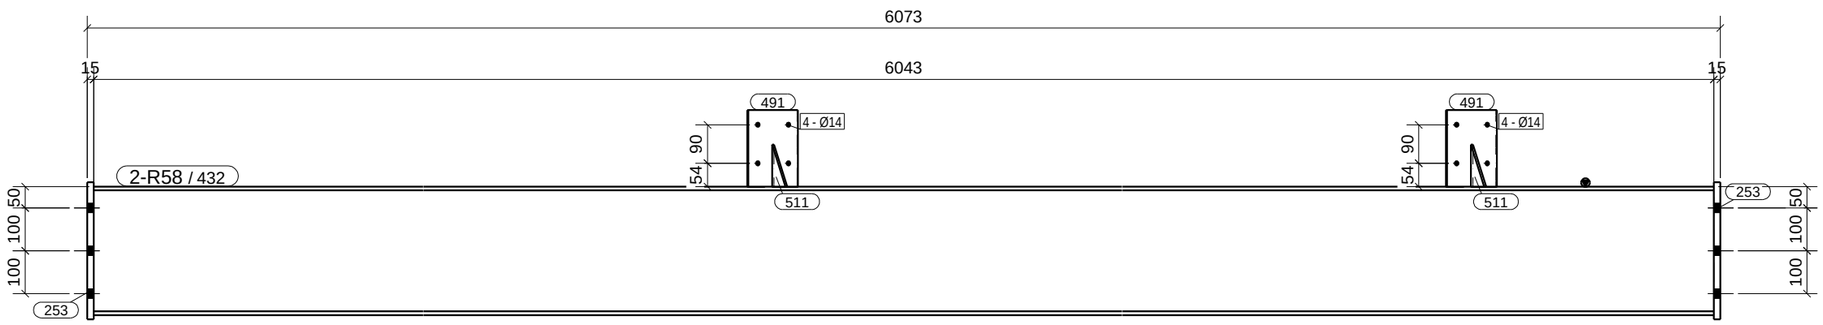

FRONT VIEW

GENERAL NOTES:

1. ALL HOLES ARE 22 mm DIA (UON).
2. ALL DIMENSIONS ARE IN MM (UON).
3. UNLESS OTHERWISE NOTED ALL FILLET WELD SIZE SHALL BE 7mm FILLET CONTINUOUS(UON)
4. RD DENOTES BASE LINE = 00

MARK: 2-R58
QTY: 1
DESC.: IPE300-J

REV.	DATE	DESCRIPTION	DRN	CHK	DSN

PROJECT NAME:

MADAR GROUP JORDAN

CONTRACTOR:

- - - - - - - - - - - - - - - - - - -

DRAWING TITLE:

RAFTER
2-R58

CHECKED BY	A.A	SCALE	
DATE	A.A	SHEET NO.	

Tekla structures
16/12/2026 * 15:34:57

PDF created with pdfFactory Pro trial version www.pdffactory.com
